

Hashem Akbari, Project Director Heat Island Group Environmental Energy Technologies Division MS 90R4000 1 Cyclotron Road Berkeley, CA 94720

Fax: 510-486-6996 e-mail: H\_Akbari@lbl.gov

October 7, 2005

Tel. 510-486-4287

To: Chris Scruton (CEC) From: Hashem Akbari

Subject: Cool Roof Colored Materials: Monthly Progress Report for September 2005

CC: Steve Wiel, Paul Berdahl, Andre Desjarlais, Nancy Jenkins, Bill Miller, Ronnen

Levinson

A summary of the status of Tasks and Deliverables as of September 30, 2005 is presented in Attachment 1.

### HIGHLIGHTS

- We are working to complete deliverables for Tasks 2.5.3 "Accelerated Weathering."
- We have completed a draft report for deliverable 2.6.3 summarizing the field testing of clay and concrete tile roofs on the steep-slope assembly at ORNL.
- George James, Leader of DOE's Building America, has shown interest for a collaborative work between LBNL and ORNL to couple their new PIER initiatives with Building America's goals. He wants the community of homes that Building America is establishing to have cool colored roofs.

### **Tasks**

- 1.1 <u>Attend Kick-Off Meeting</u> Task completed.
- 1.2 <u>Describe Synergistic Projects</u> **Task completed.**
- 2.1 <u>Establish the Project Advisory Committee (PAC)</u> **Task completed.**
- 2.2 <u>Software Standardization</u> (No activity.)
- 2.3 <u>PAC Meetings</u> **Task completed.**
- 2.4 <u>Development of Cool Colored Coatings</u>
- 2.4.1 <u>Identify and Characterize Pigments with High Solar Reflectance</u>

### Task completed.

2.4.2 <u>Develop a Computer Program for Optimal Design of Cool Coatings</u> **Task completed**.

## 2.4.3 <u>Develop a Database of Cool-Colored Pigments</u> Task completed.

- 2.5 Development of Prototype Cool-Colored Roofing Materials
- 2.5.1 Review of Roofing Materials Manufacturing Methods Task completed.
- 2.5.2 <u>Design Innovative Methods for Application of Cool Coatings to Roofing Materials</u> **Task completed**.
- 2.5.3 <u>Accelerated Weathering Testing</u>

Work on the manuscript on accelerated weathering is continuing. An extensive bibliography was compiled earlier. Recent newsletters by Atlas, Materials Testing Solutions have been identified as good sources on the current state of the art. These newsletters are proving helpful in identifying some of the best recent references out of the hundreds available.

Often (for example, especially for polymers), ultraviolet radiation is a key weathering influence. An emphasis of current research is ensuring a better match between natural UV spectra and those produced by accelerated test equipment.

Some manufacturers of roofing materials have been harshly critical of accelerated weathering testing. This just emphasizes the point that if the in-field degradation mechanisms are poorly understood, then accelerated weathering tests can be inappropriate and misleading.

Concrete corrodes due to reaction with carbon dioxide in the air. Basically, calcium hydroxide is transformed into calcium carbonate and water. (This is essentially the inverse of the manufacturing process in which CaCO<sub>3</sub> is heated to a high temperature, yielding CaO and CO<sub>2</sub>.) We located an interesting paper on the accelerated weathering of concrete by aging it in high concentrations of CO<sub>2</sub> (5% vs. 0.3% in natural air).

### 2.6 Field-Testing and Product Useful Life Testing

Miller completed a draft report for deliverable 2.6.3 summarizing the field testing of clay and concrete tile roofs on the steep-slope assembly at ORNL. The field data for the residential demonstrations at Fair Oaks and Redding CA were presented at the Building America quarterly review meeting.

2.6.1 <u>Building Energy-Use Measurements at California Demonstration Sites</u> *Tile and Painted Metal Demonstrations*: The Sacramento Municipal Utility District forwarded the summer revenue meter readings for the two pair of demonstration homes in Fair Oaks, CA (Table 1). The kWh use during the summer for the home with cool

Table 1. Revenue Mete	r Readings for Dem	onstration Home	s in Fair Oaks CA	
	Whole House F	ower (kWh)	Whole Hous	se Power (kWh)
	Metal Shake	Metal Shake	Medium-Profile Tile	Medium-Profile Tile
Date	Conventional Color	Cool Color	Conventional Color	Cool Color
6/18/05	409	552	734	993
7/20/05	1433	749	891	1511
8/18/05	1034	807	884	1412

color metal shakes was 26% less than that for the same home with conventional metal shakes. However, the cool tile used 56% more energy to comfort condition the home than did the home with standard tile. Solar reflectance of the cool tile is about 0.41 as compared to 0.08 for the standard tile and should therefore show some energy savings. However, a review of the data indicates that the homeowner with standard tile roof did not maintain the thermostat at 72°F until after August 19, 2005. The individual stated she spent part of July and August in Spain. After returning home and conditioning the house, the data for the last week of August showed the heat flux through the ceiling of the home with cool coated tile was 20% less than the heat penetrating into the conditioned space of the home with conventional tile. Occupancy habits are confounding the data. Efforts will be made to plot the daily HVAC power use against the daily average outside air-to-indoor air temperature difference to see whether a correction can be applied to the difference in thermostat settings. Florida Solar Energy Center showed good correlation using the approach and successfully corrected discrepancies between thermostat set points for two different homes.

### 2.6.2 Materials Testing at Weathering Farms in California

All samples continue to be exposed in the seven weathering sites in California.

### 2.6.3 Steep-slope Assembly Testing at ORNL

Miller completed a draft report for deliverable 2.6.3 summarizing the field testing of clay and concrete tile roofs on the steep-slope assembly at ORNL. We are in the process of reviewing and editing the paper.

Field data for the clay and concrete tile exposed on the steep-slope assembly were searched for summer days having the same solar irradiance and the same outdoor air temperature. Two days were found one with the ridge vent closed the other with the ridge vent open that had very similar outdoor air temperatures and solar irradiance. The soffitt vent was open for both summer days of field testing.

Opening the ridge vent reduced the bulk air temperature within the inclined air channel for the slate tile (SR10E83) and also for the clay (SR54E90) tile. At solar noon, the bulk air temperature near the underside of the slate tile was 10°F cooler than observed for the same slate tile with the ridge vent closed the previous summer. The effect for the S-Mission clay was about a 5°F drop in the bulk air temperature for the two different

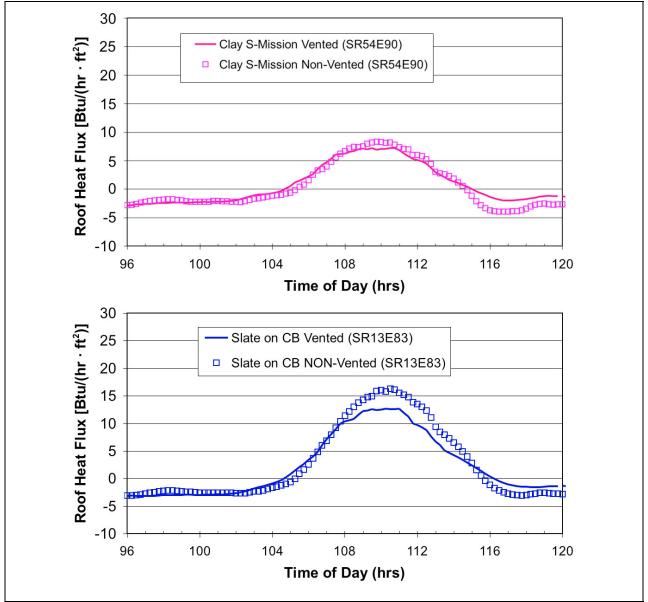


Figure 1. Heat penetrating through the roof deck of the S-Mission clay tile and the concrete slate tile with and without venting of the roof deck.

summer days having very similar weather. Slate tile are laid one atop another and have little clearance for the seepage of air between overlapped tiles. The S-Mission tiles are designed porous for minimizing wind uplift forces. Therefore the clay tile allowed more leakage of air between overlapped tiles than observed for the slate tile system. As result, opening the ridge vent caused a more significant drop in heat flow crossing the roof deck for the slate tile roof as compared to the clay tile roof (Fig. 1). The results imply that opening the ridge caused more daytime heat to be exhausted out the ridges for both the S-Mission clay and the slate tile systems. There is also another very interesting trend observed from 8 p.m. until about 4 a.m. Opening the ridge vent of both tile systems caused the bulk air temperature during the nighttime to be warmer than that observed for both systems with the ridge closed. Hence, the heat lost from the attic is reduced with the

ridge vent open (Fig. 1). The thermal mass of the tile keep them warm during the evening whether the ridge vent is open or closed. However, when colder and denser air overlays a warmer and less dense air convective roll waves begin to form that enhance heat transfer to the air on the underside of the tile. This is not the situation for the two different days of data – one with ridge venting the other without. The actual mechanism is not fully understood but is believed linked to the reason that venting alleviates ice damming in cold climates.

### 2.6.4 Product Useful Life Testing

Our review paper "Weathering of Roofing Materials-An Overview," by Berdahl, Akbari, Levinson, and Miller, was substantially completed earlier. Each of the coauthors has now provided various suggestions for improvements (e.g., more figures, more discussion of the connections between weathering generally and cool roofing specifically, more data on long-term weathering of coated metal). We expect to submit this paper to the CEC and for peer review next month. Construction and Building Materials is the prospective journal.

The Shepherd Color Company and 3M Mineral continue to expose roof samples with and without cool colored pigments to accelerated fluorescent light and Xenon-arc irradiance. Shepherd has logged over 3000 hours of QUV exposure.

### 2.7 <u>Technology transfer and market plan</u>

### 2.7.1 Technology Transfer

W. Miller presented results of the residential field demonstrations at the quarterly Building America meeting held at the Department of Energy headquarters in Washington, DC. Building America has targeted 30, 40 and 50% decreases in whole house energy for communities of homes by the dates set in Table 2. The savings are based on a benchmark that is generally consistent with mid-1990s standard practice (for specifics of the benchmark see <a href="http://www.nrel.gov/docs/fy05osti/36429.pdf">http://www.nrel.gov/docs/fy05osti/36429.pdf</a>).

Table 2. Building America Target Dates for Establishing Communities Showcasing Energy savings.

Savings	Marine	Hot Humid	Hot/Dry/Humid	Mixed	Cold
30%	2006	2007	2005	2006	2005
40%	2008	2010	2007	2008	2009
50%	2011	2015	2012	2013	2014

George James, Leader of Building America, stated he wants the LBNL and ORNL team to couple their new PIER initiatives with Building America's goals. He wants the community of homes that Building America is establishing to have cool pigmented roofs that will help meet the goals set in Table 2.

On September 13, 2005, at the Build Green San Diego conference, Akbari gave a presentation on the topic of "Potentials of Urban Heat Island Mitigation to Reduce Energy Use and Improve Air Quality in Urban Areas."

### 2.7.2 Market Plan

Task completed.

### 2.7.3 Title 24 Code Revisions

### Task completed.

### **Management Issues**

• Since the project has been extended through December 2006 to accommodate additional testing (Tasks 2.6.1, 2.6.2, and 2.6.3), Akbari and Scruton agreed to submit quarterly progress report until the completion of the project.

• We have not yet obtained the formal approval of the requested no-cost extension (through December 2006) for the project. Approval is critical for ORNL to continue work because as on October 3, 2005 all work orders are closed and no further charges incurred until a new stop date is issued by the CEC.

Page 7 October 7, 2005

Attachment 1

Project Tasks and Schedules (Approved on May 16, 2002; Revised schedules approved November 2004)

tivities         Date	Task	Task Title and Deliverables	Plan Start	Actual Start	Plan Finish	Actual Finish	% Completion as of
Preliminary Activities			Date	Date	Date	Date	9/30/2005
Attend Kick Off Meeting  Deliverables:  Initial schedule for the Project Advisory Committee meetings  Initial schedule for the Project Reviews (Completed)  Initial schedule for the Critical Project Reviews (Completed)  Describe Synegistic Projects at LBNL and ORNL (Completed)  Initial schedule for the Critical Project Reviews (Completed)  Initial schedule for the Critical Project Reviews (Completed)  Describe Synegistic Projects  Initial schedule for the Critical Project Reviews (Completed)  Describe Synegistic Projects  Initial schedule for the Critical Project Reviews (Completed)  Describe Synegistic Projects  Initial schedule for the Critical Project Reviews (Completed)  Initial schedule for the Critical Project Reviews (Completed)  Deliverables:  Proposed Initial PAC Organization Membership List (Completed)  When applicable, all reports will include additional file formats that will be necessary to transfer deliverables to the CEC  When applicable, all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables	1	Preliminary Activities					
Witten documentation of meeting agreements and all pertinent information (Completed)     Initial schedule for the Project Advisory Committee meetings     (Completed)     Initial schedule for the Project Advisory Committee meetings     (Completed)     Initial schedule for the Project Reviews (Completed)     Initial schedule for the Critical Project Reviews (Completed)     Initial schedule for the Critical Project Reviews (Completed)	1.1	Attend Kick Off Meeting	5/16/02	2/16/02	6/1/02	6/10/02	100%
<ul> <li>Written documentation of meeting agreements and all pertinent information (Completed)</li> <li>Initial schedule for the Project Advisory Committee meetings (Completed)</li> <li>Initial schedule for the Project Reviews (Completed)</li> <li>Initial schedule for the Project Reviews (Completed)</li> <li>Initial schedule for the Critical Project Reviews (Completed)</li> <li>A list of relevant on-going projects at LBNL and ORNL (Completed)</li> <li>Identify Required Permits</li> <li>Obtain Required Permits</li> <li>Identify Required Permits</li> <li>Identify Required Permits</li> <li>Obtain Required Permits</li> <li>Identify Reduired P</li></ul>		Deliverables:					
Initial schedule for the Project Advisory Committee meetings     (Completed)     • Initial schedule for the Project Advisory Committee meetings     (Completed)     • Initial schedule for the Project Reviews (Completed)     • Initial schedule for the Critical Project Reviews (Completed)     Describe Synergistic Projects     Deliverables:     • A list of relevant on-going projects at LBNL and ORNL (Completed)     Identify Required Permits     Obtain Required Permits     Prepare Production Readiness Plan     Technical Tasks     Prepare Production Readiness Plan     Technical Tasks     Deliverables:     • Proposed Initial PAC Organization Membership List (Completed)     • Finalize Initial PAC Organization Membership List (Completed)     • Pac Meeting Schedule (Completed)     • Letters of Acceptance (Completed)     • Letters of Acceptance (Completed)     • Letters of Acceptance (Completed)     • Maken applicable, all reports will include additional file formats that will be necessary to transfer deliverables     • When applicable, all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables		<ul> <li>Written documentation of meeting agreements and all pertinent</li> </ul>					
<ul> <li>Initial schedule for the Project Advisory Committee meetings (Completed)  Initial schedule for the Critical Project Reviews (Completed)  Initial schedule for the Critical Project Reviews (Completed)  Describe Syncagistic Projects  A list of relevant on-going projects at LBNL and ORNL (Completed)  Identify Required Permits Obtain Required Permits  Obtain Required Permits  Obtain Required Permits  Obtain Required Permits  Prepare Production Readiness Plan  Technical Tasks  Establish the project advisory committee  Obtain Required Permits  Obtain Required Permits  Obtain Required Permits  Proposed Initial PAC Organization Membership List (Completed)  When applicables, all reports will include additional file formats that will be necessary to transfer deliverables:  When applicable, all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables</li> </ul>		information (Completed)					
<ul> <li>(Completed)</li> <li>Initial schedule for the Critical Project Reviews (Completed)</li> <li>Initial schedule for the Critical Project Reviews (Completed)</li> <li>Describe Synegistic Projects</li> <li>A list of relevant on-going projects at LBNL and ORNL (Completed)</li> <li>Identify Required Permits</li> <li>Obtain Required Permits</li> <li>Technical Tasks</li> <li>Establish the project advisory committee</li> <li>Finalize Initial PAC Organization Membership List (Completed)</li> <li>PAC Meeting Schedule (Completed)</li> <li>Etinalize Initial PAC Organization Membership List (Completed)</li> <li>Etinalize Initial PAC Organization Membership List (Completed)</li> <li>When applicable, all reports will include additional file formats that will be necessary to transfer deliverables to the CEC</li> <li>When applicable, all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables</li> </ul>		<ul> <li>Initial schedule for the Project Advisory Committee meetings</li> </ul>					
<ul> <li>Initial schedule for the Critical Project Reviews (Completed)  Describe Synergistic Projects  Describe Synergistic Projects  Obliverables:  A list of relevant on-going projects at LBNL and ORNL (Completed)  Identify Required Permits Obtain Required Permits  Obtain Required Permits  Define Reduired Permits  Obtain Required Permits  Define Reduired Permits  Prepare Production Readiness Plan  Technical Tasks  Establish the project advisory committee  Deliverables:  Proposed Initial PAC Organization Membership List (Completed)  PAC Meeting Schedule (Completed)  PAC Meeting Schedule (Completed)  PAC Meeting Schedule (Completed)  Letters of Acceptance (Completed)  Software standardization  Deliverables:  When applicable, all reports will include additional file formats that will be necessary to transfer deliverables to the CEC  When applicable, all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables</li> </ul>		(Completed)					
Describe Synergistic Projects  Deliverables:  • A list of relevant on-going projects at LBNL and ORNL (Completed)  I dentify Required Permits  Obtain Required Permits  Technical Tasks  Establish the project advisory committee  Deliverables:  • Proposed Initial PAC Organization Membership List (Completed)  • Frailize Initial PAC Organization Membership List (Completed)  • PAC Meeting Schedule (Completed)  • PAC Meeting Schedule (Completed)  • Letters of Acceptance (Completed)  • When applicable, all reports will include additional file formats that will be necessary to transfer deliverables to the CEC  • When applicable, all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables		• Initial schedule for the Critical Project Reviews (Completed)					
<ul> <li>Deliverables:</li> <li>A list of relevant on-going projects at LBNL and ORNL (Completed)</li> <li>Identify Required Permits</li> <li>Obtain Required Permits</li> <li>Obtain Required Permits</li> <li>Obtain Required Permits</li> <li>Technical Tasks</li> <li>Establish the project advisory committee</li> <li>Establish the project advisory committee</li> <li>Deliverables:</li> <li>Proposed Initial PAC Organization Membership List (Completed)</li> <li>Finalize Initial PAC Organization Membership List (Completed)</li> <li>PAC Meeting Schedule (Completed)</li> <li>Letters of Acceptance (Completed)</li> <li>And N/A</li> <li>Software standardization</li> <li>Deliverables:</li> <li>When applicable, all reports will include additional file formats that will be necessary to transfer deliverables to the CEC</li> <li>When applicable, all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables</li> </ul>	1.2	Describe Synergistic Projects	5/1/02	2/1/02	5/1/02	5/1/02	100%
<ul> <li>A list of relevant on-going projects at LBNL and ORNL (Completed)</li> <li>Identify Required Permits</li> <li>Obtain Required Permits</li> <li>Prepare Production Readiness Plan</li> <li>Technical Tasks</li> <li>Establish the project advisory committee</li> <li>Deposed Initial PAC Organization Membership List (Completed)</li> <li>Finalize Initial PAC Organization Membership List (Completed)</li> <li>PAC Meeting Schedule (Completed)</li> <li>PAC Meeting Schedule (Completed)</li> <li>And And Marchaeting Schedule (Completed)</li> <li>And And And And And And And And And And</li></ul>		Deliverables:					
Identify Required Permits		• A list of relevant on-going projects at LBNL and ORNL (Completed)					
Obtain Required Permits Prepare Production Readiness Plan  Technical Tasks  Establish the project advisory committee  Deliverables:  Proposed Initial PAC Organization Membership List (Completed) Finalize Initial PAC Organization Membership List (Completed) Finalize Initial PAC Organization Membership List (Completed) PAC Meeting Schedule (Completed)  Letters of Acceptance (Completed) Letters of Acceptance (Completed)  Letters of Acceptance (Completed)  M/A  Software standardization Deliverables: When applicable, all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables  When applicables all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables	1.3	Identify Required Permits	N/A		N/A		
<ul> <li>Technical Tasks</li> <li>Establish the project advisory committee</li> <li>Establish the project advisory committee</li> <li>Deliverables: <ul> <li>Finalize Initial PAC Organization Membership List (Completed)</li> <li>Finalize Initial PAC Organization Membership List (Completed)</li> <li>Finalize Initial PAC Organization Membership List (Completed)</li> <li>Etters of Acceptance (Completed)</li> <li>Letters of Acceptance (Completed)</li> </ul> </li> <li>Software standardization <ul> <li>Deliverables:</li> <li>When applicable, all reports will include additional file formats that will be necessary to transfer deliverables to the CEC</li> <li>When applicable, all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables</li> </ul> </li> </ul>	1.4	Obtain Required Permits	N/A		N/A		
Technical Tasks       Februical Tasks         Establish the project advisory committee       6/1/02       5/17/02       9/1/02         Deliverables: <ul> <li>Proposed Initial PAC Organization Membership List (Completed)</li> <li>Finalize Initial PAC Organization Membership List (Completed)</li> <li>Letters of Acceptance (Completed)</li> </ul> N/A     N/A         Software standardization       Deliverables:	1.5	Prepare Production Readiness Plan	N/A		N/A		
Establish the project advisory committee  Deliverables:  Proposed Initial PAC Organization Membership List (Completed)  Finalize Initial PAC Organization Membership List (Completed)  PAC Meeting Schedule (Completed)  Letters of Acceptance (Completed)  Software standardization  Deliverables:  When applicable, all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables  Pi//02 9/1/02 9/1/02 9/1/02 9/1/02 9/1/02	2	Technical Tasks					
<ul> <li>Deliverables:</li> <li>Proposed Initial PAC Organization Membership List (Completed)</li> <li>Finalize Initial PAC Organization Membership List (Completed)</li> <li>PAC Meeting Schedule (Completed)</li> <li>Letters of Acceptance (Completed)</li> <li>Software standardization</li> <li>Software standardization</li> <li>When applicable, all reports will include additional file formats that will be necessary to transfer deliverables to the CEC</li> <li>When applicable, all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables</li> </ul>	2.1	Establish the project advisory committee	6/1/02	2/11/02	9/1/02	9/1/02	100%
<ul> <li>Proposed Initial PAC Organization Membership List (Completed)</li> <li>Finalize Initial PAC Organization Membership List (Completed)</li> <li>PAC Meeting Schedule (Completed)</li> <li>Letters of Acceptance (Completed)</li> <li>Software standardization</li> <li>Deliverables: <ul> <li>When applicable, all reports will include additional file formats that will be necessary to transfer deliverables to the CEC</li> <li>When applicable, all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables</li> </ul> </li> </ul>		Deliverables:					
<ul> <li>Finalize Initial PAC Organization Membership List (Completed)</li> <li>PAC Meeting Schedule (Completed)</li> <li>Letters of Acceptance (Completed)</li> <li>Software standardization</li> <li>Deliverables:</li> <li>When applicable, all reports will include additional file formats that will be necessary to transfer deliverables to the CEC</li> <li>When applicable, all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables</li> </ul>		<ul> <li>Proposed Initial PAC Organization Membership List (Completed)</li> </ul>					
<ul> <li>PAC Meeting Schedule (Completed)</li> <li>Letters of Acceptance (Completed)</li> <li>Software standardization  Deliverables: <ul> <li>When applicable, all reports will include additional file formats that will be necessary to transfer deliverables to the CEC</li> <li>When applicable, all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables</li> </ul> </li> </ul>		• Finalize Initial PAC Organization Membership List ( <b>Completed</b> )					
<ul> <li>Letters of Acceptance (Completed)</li> <li>Software standardization  Deliverables: <ul> <li>When applicable, all reports will include additional file formats that will be necessary to transfer deliverables to the CEC</li> <li>When applicable, all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables</li> </ul> </li> </ul>		• PAC Meeting Schedule (Completed)					
Software standardization  Deliverables:  When applicable, all reports will include additional file formats that will be necessary to transfer deliverables to the CEC  When applicable, all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables		• Letters of Acceptance (Completed)					
<ul> <li>Deliverables:</li> <li>When applicable, all reports will include additional file formats that will be necessary to transfer deliverables to the CEC</li> <li>When applicable, all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables.</li> </ul>	2.2	Software standardization	N/A		N/A		
<ul> <li>When applicable, all reports will include additional file formats that will be necessary to transfer deliverables to the CEC</li> <li>When applicable, all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables</li> </ul>		Deliverables:					
<ul> <li>be necessary to transfer deliverables to the CEC</li> <li>When applicable, all reports will include lists of the computer platforms, operating systems and software required to review upcoming software deliverables</li> </ul>		• When applicable, all reports will include additional file formats that will					
When applicable, all reports will include lists of the computer platforms,     operating systems and software required to review upcoming software     deliverables		be necessary to transfer deliverables to the CEC					
		• When applicable, all reports will include lists of the computer platforms,					

Page 8 October 7, 2005

# Project Tasks and Schedules (contd.)

Task	Task Title and Deliverables	Plan	Actual	Plan	Actual	% Completion
		Start Date	Start Date	Finish Date	Finish Date	as of 9/30/2005
2.3	PAC meetings (Completed)  Deliverables:	9/1/02	6/1/02	6/1/05		100% (6/6)
	<ul> <li>Draft PAC meeting agenda(s) with back-up materials for agenda items</li> </ul>					
	<ul> <li>Final PAC meeting agenda(s) with back-up materials for agenda items</li> <li>Schedule of Critical Project Reviews Draft PAC Meeting Summaries</li> <li>Final PAC Meeting Summaries</li> </ul>					
2.4	Development of cool colored coatings					
2.4.1	Identify and Characterize Pigments with High Solar Reflectance Deliverables:	6/1/02	6/1/02	12/1/04	12/31/04	100%
	<ul> <li>Pigment Characterization Data Report (Completed)</li> </ul>			12/31/04		
2.4.2	Develop a Computer Program for Optimal Design of Cool Coatings Deliverables:	11/1/03	11/1/03	$12/1/04$ $\rightarrow 5/1/05$	2/30/02	100%
	<ul> <li>Computer Program (Completed)</li> </ul>					
2.4.3	Develop a Database of Cool-Colored Pigments $Deliverables$ :	6/1/03	7/1/03	6/1/05 <b>→</b> 12/31/04	12/31/04	100%
	• Electronic-format Pigment Database (Completed)					
2.5	Development of prototype cool-colored roofing materials					
2.5.1	Review of Roofing Materials Manufacturing Methods Deliverables:	6/1/02	6/1/02	6/1/03	4/1/05	100%
	<ul> <li>Methods of Fabrication and Coloring Report (Completed)</li> </ul>					
2.5.2	Design Innovative Methods for Application of Cool Coatings to Roofing Materials  Deliverables:	6/1/02	6/1/02	12/1/04 → 5/1/05	50/08/9	$\sim 100\%$
	<ul> <li>Summary Coating Report (Completed)</li> <li>Prototype Performance Report (Completed)</li> </ul>					
2.5.3	Accelerated Weathering Testing  Deliverables:	11/1/02	10/1/02	6/1/05 <b>→</b> 10/1/05		~ 85%
	Accelerated Weathering Lesting Report					

Page 9 October 7, 2005

# Project Tasks and Schedules (contd.)

Task	Task Title	Plan	Actual	Plan	Actual	% Completion
		Start Date	Start Date	Finish Date	Finish Date	as ot 9/30/2005
2.6	Field-testing and product useful life testing					
2.6.1	Building Energy-Use Measurements at California Demonstration Sites	6/1/02	9/1/02	10/1/05		93%
	• Demonstration Site Test Plan (Completed)			10/1/06		
	• Test Site Report					
2.6.2	Materials Testing at Weathering Farms in California	6/1/02	10/1/02	10/1/05		%06
	<ul> <li>Weathering Studies Report</li> </ul>			10/1/06		
2.6.3	Steep-slope Assembly Testing at ORNL Deliverables:	6/1/02	10/1/02	10/1/05		95%
	Whole-Building Energy Model Validation					
	Presentation at the Pacific Coast Builders Conference					
	Steep Slope Assembly Test Report					
2.6.4	Product Useful Life Testing  Deliverables:	5/1/04	5/1/04	€/1/05		%86
	Solar Reflectance Test Report (Draft Prepared)			10/1/05		
2.7	Technology transfer and market plan					
2.7.1	Technology Transfer ( <b>Completed</b> )  Deliverables:	6/1/03	70/1/9	9/1/9	6/1/05	100%
	Publication of results in industry magazines and refereed journal articles					
	Participation in buildings products exhibition, such as the PCBC Brochure summarizing research results and characterizing the benefits of cool colored					
	rooting materials	:		:		
2.7.2	Market Plan Deliverables:	5/1/05	4/1/05	6/1/05	7/10/05	100%
	• Market Plan(s) (Completed)					
2.7.3	Title 24 Code Revisions  Deliverables:	6/1/02	5/16/02	6/1/05	9/30/02	100%
	Document coordination with Cool Roofs Rating Council in monthly progress reports (Completed)					
	• Title 24 Database (Completed)					

Page 10 October 7, 2005

Project Tasks and Schedules (contd.)

Task	Task Title	Plan	Actual	Plan	Actual	% Completion
		Start Date	Start	Finish	Finish	as of
			Date	Date	Date	9/30/2005
VIII	Critical Project Review(s)					
	Deliverables:					
	<ul> <li>Minutes of the CPR meeting</li> </ul>					
XIII	Monthly Progress Reports	6/1/02	6/1/02	6/1/05		112% (40/36)
<u>O</u>	Deliverables:					
	<ul> <li>Monthly Progress Reports (Completed)</li> </ul>					
XIII	Final Report	3/1/05 →		10/1/05		
<u>(</u>	Deliverables:	3/31/06		<b>↑</b>		
	Final Report Outline			10/1/06		
	Final Report					
	Final Meeting	10/15/05		10/31/05		
	Deliverables:					
	<ul> <li>Minutes of the final meeting</li> </ul>					

## Appendix A Accelerated Fluorescent Light Test Data

Shepherd Color Company is conducting the fluorescent light exposure testing according to ASTM G154-04 using a 340 nm lamp for daylight UV irradiance. Exposure conditions are 8 hours of UV light at 60°C black panel temperature followed by 4 hours of condensation at 50°C. Total color change is measured using a Hunter Labscan instrument. Solar reflectance is measured using the Device & Services reflectometer. Gloss is measured using a BYK Gardner Micro-TRI-gloss device.

Table A1. Solar reflectance, Total Color Change and the Gloss of Roof Samples Exposed to Fluorescent Light at Shepherd Color Company.

			Initial M	easures	1000 hours of	f Fluorescent li	ght exposure	2000 hours of	Fluorescent li	ght exposure
			Solar		Solar			Solar		
	Material Code	Roof Product	Reflectance	Gloss	Reflectance	Total ∆E	Gloss	Reflectance	Total ∆E	Gloss
	Natural Red Cool 140	Clay tile	44.6	2.0	44.6	1.4	2.0	45.0	0.5	2.0
	Natural Red Cool 141	ĺ	44.8	2.0	45.0	0.8	2.0	45.0	0.3	2.0
	Natural Red Cool 142		44.7	2.0	44.6	0.7	2.0	45.0	0.7	2.0
	Ironwood Cool 146		25.9 i	1.0	25.9	0.2	1.0	26.0	0.2	1.0
	Ironwood Cool 147		27.3 i	1.0	26.8	0.5	1.0	27.0	0.5	1.0
	Ironwood Cool 148	<b>*</b>	26.7	1.0	26.4	0.5	1.0	26.0	0.6	1.0
872	T3 Slate Bronze Cool 124	PVDF Metal	26.0	28.0	25.8	0.3	29.0	26.0	0.5	29.0
872	T3 Slate Bronze Cool 125	1	25.9	28.0	25.7	0.4	28.0	26.0	0.7	27.0
872	T3 Slate Bronze Cool 126		25.9	28.0	25.8	0.3	29.0	26.0	0.5	29.0
815T	119 Slate Bronze Std 127		11.7	28.0	11.7	0.4	28.0	12.0	0.6	28.0
87	2R10 Brick Red Cool 112		36.7	36.0	36.0	0.3	36.0	35.0	1.2	36.0
87	2R10 Brick Red Cool 113		36.6	37.0	36.3	0.2	37.0	36.0	0.3	37.0
87	2R10 Brick Red Cool 114		36.6	36.0	36.2	0.3	37.0	36.0	0.4	36.0
8	15R71 Brick Red Std 115	<b>Y</b>	19.0	29.0	19.2	0.8	30.0	19.0	0.8	30.0
	Terracotta M3308	Concrete tile	30.8	8.0	30.1	1.7	9.0	30.0	1.6	7.0
	Terracotta IR3308		46.9	11.0	45.9	1.6	14.0	46.0	1.3	6.0
	Chocolate M3808		12.9	4.0	12.1	1.3	4.0	12.0	1.3	4.0
	Chocolate IR3808	*	39.2	12.0	38.2	1.6	12.0	38.0	1.9	7.0
		Asphalt Shingle	25.8	0.0	25.5	0.8	0.0	26.0	1.0	0.0
	Cool IRR - A2	1	25.3	0.0	24.6	1.8	0.0	25.0	1.1	0.0
	Std - B1		6.7	0.0	7.2	1.3	0.0	7.0	1.6	0.0
	Std - B2		7.4	0.0	7.7	0.3	0.0	8.0	0.2	0.0
	Cool - C1		26.9 i	0.0	26.8	2.0	0.0	27.0	1.8	0.0
	Cool - C2		26.1	0.0	25.2	2.5	0.0	25.0	1.2	0.0
	Std - D1		10.0	0.0	10.5	1.2	0.0	11.0	0.7	0.0
	Std - D2		11.3	0.0	11.5	0.2	0.0	11.0	0.9	0.0
	Std Premium - E1		6.5	0.0	6.8	1.1	0.0	8.0	2.3	0.0
	Std Premium - E2		6.5	0.0	6.4	1.0	0.0	7.0	1.8	0.0
	Cool Premium - F1		23.6	0.0	23.8	0.6	0.0	24.0	0.3	0.0
	Cool Premium - F2	•	25.0	0.0	23.8	0.6	0.0	25.0	0.6	0.0

<sup>\*</sup>A1,61,C1,U1,E1,F1 are samples of asphalt shingles cut from valley of shingle \*A2,B2,C2,D2,E2,F2 are samples of asphalt shingles cut from tooth of shingle \*Premium refers to a top-of-the-line shingle having a 50 year warranty

 American Society for Testing and Materials (ASTM). 2005. Designation G 154-04: Standard Practice for Operating Fluorescent Light Apparatus for UV Exposure of Nonmetallic Materials. West Conshohocken, Pa.: American Society for Testing and Materials.

### Appendix A Xenon-Arc Exposure Test Data

Xenon-arc exposure testing is \being conducted according to ASTM G155-04a. A daylight filters is used to simulate daylight UV irradiance. The exposure conditions require 102 minutes of light at 63°C black panel temperature followed by 18 minutes of light with condensation. Panel temperature is not controlled during condensation. A radiometer monitors the irradiance and the measurement is used in a feed back control loop to control the radiant energy incident on the samples. Total color change is measured using a Hunter Labscan instrument. Solar reflectance is measured using the Device & Services reflectometer. Gloss is measured using a BYK Gardner Micro-TRI-gloss device.

Table A2. Solar Reflectance, Total Color Change And Gloss Of Roof Samples Exposed To Xenon-Arc Exposure At 3M Minerals Company.

			Initial M	easures		of Xenon-Arc	exposure		of Xenon-Ar	c exposure
			Solar		Solar			Solar		
	Material Code	Roof Product	Reflectance	Gloss	Reflectance	Total ∆E	Gloss	Reflectance	Total ∆E	Gloss
	Natural Red Cool 240	Clay tile	43.3	1.8	44.2	5.5	1.3	43.6	3.4	1.2
	Natural Red Cool 241		43.5	1.9	40.4	9.9	1.7	37.9	6.5	1.7
	Natural Red Cool 242		43.8	1.8	36.7	7.7	1.4	34.4	8.7	1.3
	Ironwood Cool 246		25.5	0.6	20.6	6.8	0.5	21.0	6.1	0.5
	Ironwood Cool 247		26.5	0.6	27.5	1.5	0.6	27.4	1.8	0.6
	Ironwood Cool 248	*	25.8	0.6	23.6	4.4	0.5	24.1	4.3	0.5
872	T3 Slate Bronze Cool 224	PVDF Metal	25.3	29.3	26.6	0.2	29.3	26.6	0.7	27.4
872	2T3 Slate Bronze Cool 225	1	25.3	29.0	26.5	0.2	28.9	26.7	0.8	27.1
872	2T3 Slate Bronze Cool 226		25.2	27.2	26.4	0.3	27.1	26.7	0.6	26.1
815T	119 Slate Bronze Std 227		11.5	29.6	11.7	0.2	28.9	12.0	0.3	27.9
87	72R10 Brick Red Cool 212		35.9	37.6	37.4	0.3	36.9	37.5	0.5	35.4
87	72R10 Brick Red Cool 213		36.0	37.3	37.6	0.2	37.3	37.6	0.6	36.1
87	72R10 Brick Red Cool 214		35.8	37.4	37.5	0.2	36.8	37.6	0.5	35.7
8	315R71 Brick Red Std 215	•	18.6	29.8	19.2	0.1	30.6	19.6	0.7	29.5
	Terracotta M3308	Concrete tile	29.9	12.6	30.6	2.7	12.8	30.7	2.9	13.5
	Terracotta IR3308		45.4	6.3	46.7	2.0	6.3	46.9	2.8	5.7
	Chocolate M3808		12.3	4.7	12.1	1.2	5.5	12.3	1.5	5.8
	Chocolate IR3808	+	38.4	5.1	39.6	1.2	5.4	39.6	1.7	4.9
	Cool IRR - A1	Asphalt Shingle	27.2	0.4	28.0	0.5	0.4	28.4	1.7	0.4
	Cool IRR - A2		26.3	0.4	26.3	0.8	0.3	27.4	0.9	0.4
	Std - B1		8.6	0.2	8.6	1.7	0.2	9.5	1.7	0.2
	Std - B2		8.0	0.3	8.1	1.5	0.2	8.5	1.6	0.1
	Cool - C1		27.3	0.4	28.5	1.7	0.5	29.8	1.8	0.5
	Cool - C2		26.3	0.3	27.7	1.3	0.3	27.9	1.2	0.4
	Std - D1		12.3	0.4	12.2	0.6	0.3	12.7	1.2	0.3
	Std - D2		12.1	0.3	12.1	0.9	0.3	13.2	1.2	0.4
	Std Premium - E1		6.8	0.2	7.0	0.4	0.3	7.6	2.1	0.4
	Std Premium - E2		6.7	0.3	6.8	0.7	0.3	7.4	0.7	0.4
	Cool Premium - F1		25.1	0.4	26.2	0.2	0.6	27.1	0.3	0.4
	Cool Premium - F2	*	27.4	0.5	28.3	0.8	0.5	29.2	0.7	0.4

<sup>1</sup>A1,B1,C1,D1,E1,F1 are samples of asphalt shingles cut from valley of shingle <sup>2</sup>A2,B2,C2,D2,E2,F2 are samples of asphalt shingles cut from tooth of shingle

<sup>3</sup>Premium refers to a top-of-the-line shingle having a 50 year warranty

 American Society for Testing and Materials (ASTM). 2005. Designation G 155-04a: Standard Practice for Operating Xenon Arc Light Apparatus for Exposure of Nonmetallic Materials. West Conshohocken, Pa.: American Society for Testing and Materials.
